

ARCHITECT REVIEW

SCC-3385 | Create Work Order for Tickets

Great Plains Merge to UAT | Source retrieval and check-only readiness assessment

Source	GreatPlainsMerge Org 00DEa00000GkAsHMAV
Target	GreatPlainsUAT Org 00DEa00000FZILBMA1
Review date	26 August 2026
Check-only	Failed Job 0AfEa00000bbQXhKAM 6/14 validated
Decision	NO-GO - Changes Requested before promotion
Boundary	No records, deployment, activation, or org metadata were changed

ARCHITECT DECISION


Do not promote SCC-3385. UAT lacks the Trouble Ticket foundation, the source Order exception is incomplete, WorkOrder layouts omit the new fields, and the check-only package failed 8 of 14 components.

Acceptance outcome

#	Scope	Result	Evidence
1	Action visibility	Partial fail	Source layout contains Create Work Order; UAT has no Trouble Ticket record type, so visibility cannot validate.
2	Inherited details	Partial fail	Flow maps Account, address, service, report, notes, and priority; target dependencies and WorkOrder layout fields are missing.
3	Required inputs	Static pass	Flow requires Work Type and Work Instructions. UAT has all four named trouble Work Types.
4	Duplicate prevention	Static pass	Flow checks Caseld and links the existing Work Order; Source_Case_Id__c is unique. Runtime is untested.
5	Case activity logging	Static pass	Flow creates a completed Task with Work Order number and Work Type. Runtime is untested.
6	Book Appointment	Static pass	FSL_Book_Appointment remains on the FSL layout; no runtime regression was executed.

Deployment readiness path

The source implementation is visible, but the promotion path breaks on prerequisite metadata, broad profile drift, and unresolved source design defects.

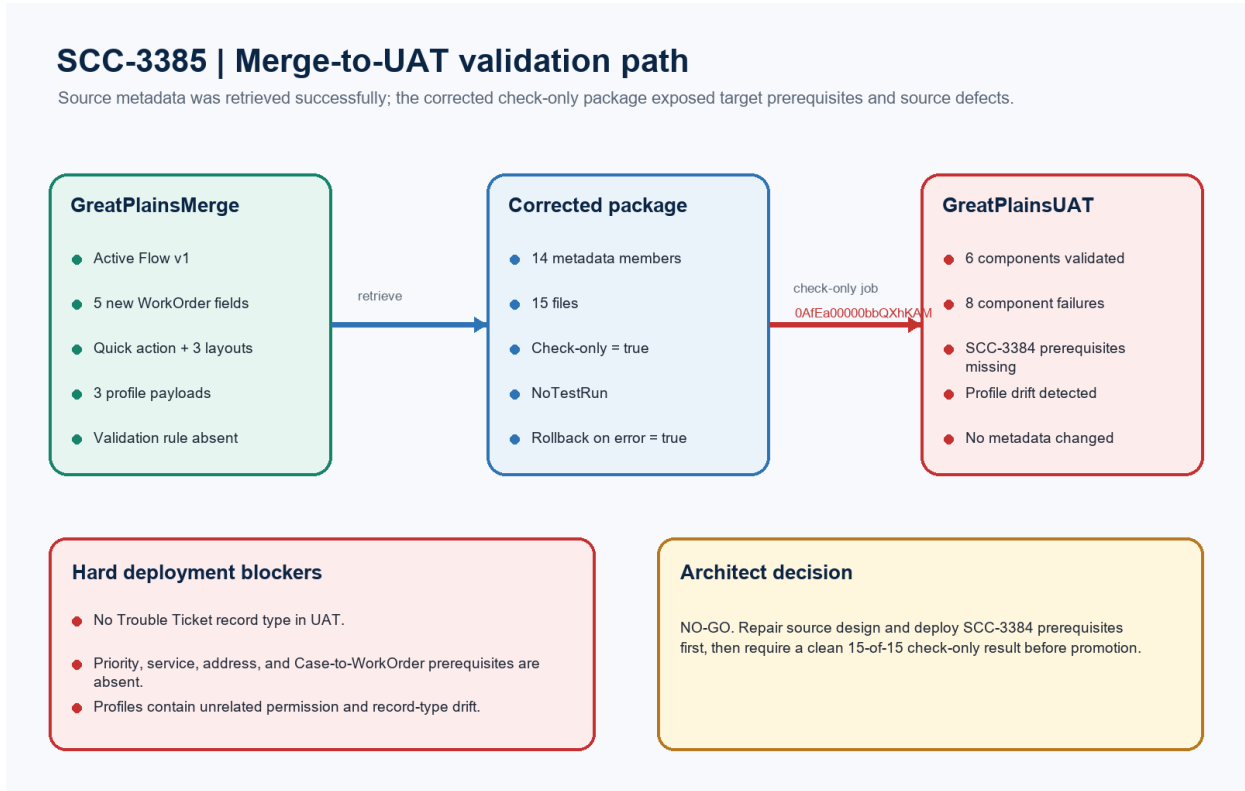

Detailed dry-run findings

1. Check-only deployment evidence

Metric	Result	Evidence
Job	0AfEa00000bbQXhKAM	checkOnly=true; rollbackOnError=true; NoTestRun
Payload	14 components / 15 files	1 Flow, 1 Quick Action, 6 fields, 3 layouts, 3 profiles
Validated	6	All six WorkOrder field members validated; five are new and Order__c is changed.
Failed	8	Flow, Quick Action, three layouts, and three profiles failed.
Tests	0	No Apex in scope; functional story tests require controlled record writes.

2. Exact failure groups

Failure group	Affected	Exact blocker
Missing Case prerequisites	4 components	Service Address, Priority__c, Case-to-WorkOrder relationship, and Trouble Ticket record type are absent in UAT.
Profile drift	3 profiles	Admin and API profile use unknown ArchiveArticles; Standard references the missing Trouble Ticket record type.
Quick Action cross-reference	1 action	Case.Create_Work_Order cannot resolve its Flow because the referenced Flow fails validation.

3. Source and story defects

Area	Status	Evidence
Order exception	Blocker	Order__c remains required=true; WorkOrder.Order_Required_Except_Trouble_Ticket does not exist.
WorkOrder layouts	Changes requested	Neither updated WorkOrder layout includes the five new SCC-3385 fields.
Component names	Correct story	Actual action is Case.Create_Work_Order; profile API names are Admin, Standard, and System Administrator - API Only.
Named Cases	Blocked	Cases 00001082 and 00001083 exist in neither authorized Great Plains sandbox.
Work Types	Ready in UAT	Comm Fiber, Resi Coax, Resi Copper, and Resi Fiber Trouble all exist in UAT.

Work Order creation architecture

The Flow contains most behavioral controls, but the target foundation and two source-side design elements prevent a complete end-to-end release.

SCC-3385 | Work Order creation model

Case prerequisites, screen Flow controls, Work Order output, and release blockers

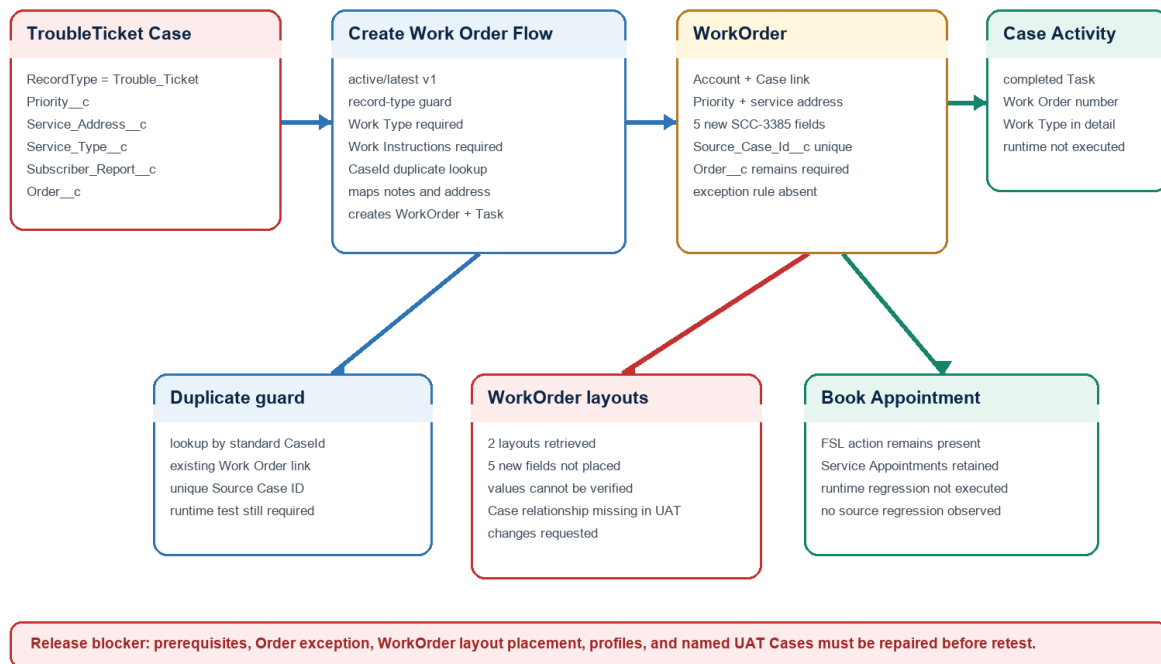


Figure 2. SCC-3385 Work Order creation and dependency model

Architect interpretation: the Flow design covers gating, required inputs, duplicate detection, value mapping, and activity logging, but deployment and runtime acceptance remain blocked until the foundation and source defects are repaired.

Required approval gates

Gate	Required action	Owner	Evidence needed
1	Deploy SCC-3384 prerequisites	Release manager	Trouble Ticket record type plus Priority, Service Address, Service Type, Subscriber Report, and Work Order Case fields.
2	Repair the Order exception	Admin / Architect	Make Order__c optional and add the active exception validation rule for non-Trouble Ticket Work Orders.
3	Complete WorkOrder layouts	Salesforce admin	Place all five new fields on both WorkOrder layouts and retain Book Appointment.
4	Narrow security payload	Security owner	Use a focused permission set or filtered profiles; remove ArchiveArticles and unrelated record-type drift.
5	Prepare named UAT Cases	QA / Business	Create or identify Cases 00001082/00001083 equivalents with exact Account, address, service, report, priority, and notes.
6	Revalidate and execute UAT	QA / Release manager	Require a clean 15/15 check-only result, then execute all six tests with IDs and screenshots.

Ready-to-paste architect response

STORY COMMENT

Architect dry run completed for SCC-3385 using GreatPlainsMerge as source and GreatPlainsUAT as the check-only target. Changes Requested / NO-GO: job 0AfEa00000bbQXhKAM was check-only and failed with 8 of 14 components; no metadata or records were changed. UAT is missing the Trouble Ticket record type and the SCC-3384 Case fields used by the Flow. In source, WorkOrder.Order__c remains required, the listed exception validation rule does not exist, and neither WorkOrder layout contains the five new fields. The Flow otherwise includes the record-type guard, required Work Type and Work Instructions, duplicate lookup/link, Case value mapping, completed Task logging, and the FSL Book Appointment action remains present. Complete the six approval gates above, prepare valid test Cases, and require a clean 15-of-15 validation plus all six UAT tests before promotion.

Evidence boundary

This assessment combines source metadata retrieval, local structural review, read-only org queries, and a GreatPlainsUAT check-only deployment. No records, deployment, activation, quick deploy, or org metadata changes were performed.
